UNIFY

Universal AI Implementation Engine

Complete Product Vision, Strategy & Technical Blueprint

Consolidated stakeholder document covering the product vision, market focus, users, core promise, PRD, architecture, database design, AI agents, workflows, APIs, security, backlog, dashboard, delivery plan and validation assumptions.

PRODUCT	INITIAL MARKET	FIRST PROTOTYPE	HORIZON
Commercial AI SaaS	ERP SaaS vendors	ERP implementation	Indicative 6 months

1. Product vision

Build an independent commercial AI platform that helps software vendors automate the customer implementation lifecycle. UNIFY connects to a vendor's product, learns its documented capabilities and implementation rules, then coordinates approved work across discovery, planning, data migration, configuration, integration, testing and go-live readiness.

Vision statement

Any company offering a configurable B2B software product should be able to connect that product to UNIFY, onboard a customer and automate a substantial share of repeatable implementation work—without rebuilding the implementation engine for every product.



Governed workflow with human approval at material decision points

Core design principle: a common implementation engine with configurable product adapters and industry-specific knowledge packs. The platform should be reusable, governed and capable of learning from approved implementation outcomes.

2. Initial market, primary user and core promise

Initial market

Start with ERP SaaS vendors that repeatedly onboard business customers and operate structured implementation teams. ERP is a demanding but practical first proving ground because it combines master data, business rules, configuration, integrations, testing and reconciliation.

Market segment	Potential implementation work
ERP SaaS	Customer/vendor/item masters, chart of accounts, opening balances, modules, configuration and testing.
WMS	Warehouse, SKU, bin, inventory and barcode setup; data synchronization.
Logistics SaaS	Customer, carrier, route, tracking and order integrations.
CRM SaaS	Customer/contact data, workflows, permissions and integrations.
Fintech software	Customer/account setup, payment connectivity, controls and transaction testing.
Manufacturing software	BOM, routing, material master, production and quality setup.

Primary customer and users

Primary buyer: B2B ERP/SaaS product vendors with recurring implementations, repeatable configuration patterns and accessible APIs or controlled integration methods.

User	Responsibility
ERP Vendor Admin	Register products, connectors, capabilities, playbooks and vendor users.
Implementation Manager	Own scope, plan, milestones, risks, approvals and go-live readiness.
Implementation Consultant	Review requirements, coordinate execution and resolve exceptions.
Data Migration Specialist	Approve mappings, transformations, migration runs and reconciliation.
QA Specialist	Review and execute test scenarios; manage defects and evidence.
Customer Admin	Submit requirements and data; review information and provide approvals.
Customer Business User	Participate in UAT and business sign-off.

Core promise

One engine. Any product. Automated implementation.

UNIFY should reduce repetitive manual effort and implementation variability by converting repeatable activities into reusable AI-assisted workflows and controlled execution tools. It should execute work—not merely recommend tasks or display project status.

Document structure

This blueprint covers: (1) Product Requirements Document; (2) functional modules and user journeys; (3) technical solution architecture; (4) database design; (5) AI agent architecture and workflows; (6) API and integration framework; (7) security and governance; (8) development backlog; (9) testing and acceptance criteria; (10) delivery roadmap; and (11) assumptions requiring validation.

PART A — PRODUCT REQUIREMENTS DOCUMENT

3. Product overview and objectives

Attribute	Definition
Product name	UNIFY – Universal AI Implementation Engine
Category	AI-powered implementation automation SaaS
Primary customer	ERP software vendors
End users	Vendor implementation teams and their customers
Deployment	Multi-tenant cloud SaaS; enterprise private deployment can follow
First supported product	One ERP SaaS product through a product adapter
AI approach	Specialized agents coordinated by durable workflows
Execution model	Human-supervised, policy-controlled execution

Problem statement

ERP vendors often rely on consultants to gather requirements, create plans, chase spreadsheets, cleanse and map data, configure modules, coordinate integrations, test scenarios and prepare go-live. Many activities recur across customers but are executed manually and inconsistently. UNIFY aims to standardize and automate eligible repeatable work while retaining human judgement for exceptions and material decisions.

Product objectives and proposed measures

Objective	MVP evidence
Requirement discovery	Structured requirements baseline with source references and review status.
Project planning	Dependency-aware plan generated from approved scope.
Data quality	Profiling report identifies defined missing, duplicate and invalid data.
Field mapping	Reviewable source-to-target mappings with rationale and confidence indicator.
Migration	Approved sandbox migration with record-level traceability and reconciliation.
Configuration	Supported configuration actions executed and verified through connector.
Testing	Requirement-linked scenarios run with evidence and pass/fail results.
Go-live readiness	Evidence-based checklist showing blockers and approvals.

4. Product scope

In scope: vendor registration and tenant setup; ERP product registration; connector configuration; customer onboarding; requirements analysis; implementation project generation; Excel/CSV ingestion; data profiling; AI-assisted field mapping; deterministic transformation and validation; sandbox migration; supported ERP configuration; basic REST API integration; test generation/execution; dashboards; approvals; audit logs; exception handling; readiness assessment.

Out of scope for first release: universal support for every ERP; fully autonomous production go-live; complex legacy UI automation; extensive banking/payment connector library; a complete ERP application; replacement of CRM/project management tools; autonomous financial approvals; full support ticketing product.

5. User roles and permissions

Role	Responsibilities
UNIFY Platform Super Admin	Platform operations, tenant lifecycle and global policies.
ERP Vendor Admin	Product registry, connector setup, users and vendor settings.
Implementation Manager	Projects, scope, milestones, risks and approvals.
Implementation Consultant	Requirements, project execution and exception resolution.
Data Migration Specialist	Mappings, validation rules, migration and reconciliation.
QA Specialist	Test scenarios, execution and quality sign-off.
Customer Admin	Customer data, requirements, invitations and approvals.
Customer Business User	UAT participation and business acceptance.

Permissions must be configurable at tenant, project, environment and action level. Backend authorization—not UI visibility alone—must enforce every permission.

6. Core functional modules

Module 01 Vendor and product management

Register vendor, ERP product/version, modules, entities, fields, capabilities, validation rules, API credentials, environments, templates and playbooks.

Output: registered product profile and usable product adapter.

Module 02 Customer onboarding

Capture company, industry, legal entities, branches, required modules, users, source systems, target dates, documents and approvals.

Output: structured customer implementation profile.

Module 03 AI requirement discovery

Process documents/spreadsheets; classify requirements; identify standard features, gaps, dependencies and customization requests; generate clarification questions and fit-gap analysis; obtain consultant approval.

Output: approved requirement baseline.

Module 04 Implementation planning

Select product playbook; generate phases, tasks, dependencies, owners, milestone dates, risks and blockers; request manager approval.

Output: approved customer-specific project plan.

Module 05 Data migration

Initial entities: customer, vendor, item, chart of accounts, branch/location and opening balances. Upload Excel/CSV; detect schema; profile; map; transform; validate; preview; approve; migrate to sandbox; reconcile; report exceptions.

Output: traceable sandbox migration with reconciliation.

Module 06 ERP configuration

Derive configuration from approved requirements; check capabilities/dependencies; propose values; obtain authorization; execute through APIs; read back and verify.

Output: verified customer-specific configuration.

Module 07 Integration management

Register external systems; securely reference credentials; configure REST/webhooks/SFTP; map fields; test connectivity; validate requests/responses; retry recoverable failures.

Output: tested integration connection and report.

Module 08 Testing and go-live

Generate requirement-linked tests; execute supported scenarios; capture evidence; record defects; retest; check migration/configuration/integration/UAT/access readiness; obtain sign-offs.

Output: evidence-based go-live readiness report.

PART B — USER JOURNEYS AND WORKFLOWS

7. End-to-end implementation journey

The orchestration engine controls project state, dependencies, approvals and recovery; agents perform bounded tasks within that workflow.



Governed workflow with human approval at material decision points

Stage	Activities	Output
1 Vendor/product setup	Register vendor, ERP product, modules, connector, sandbox and capabilities.	Configured product profile
2 Customer onboarding	Capture customer profile, scope, modules, users, documents and dates.	Customer project record
3 Discovery/planning	Extract requirements, identify fit-gap and questions, generate dependencies and plan.	Approved requirements and plan
4 Migration/configuration	Profile files, map fields, validate, transform, migrate to sandbox and configure.	Migration/configuration evidence
5 Testing/approvals	Run scenarios, reconcile outcomes, resolve exceptions and obtain sign-offs.	Test evidence and approvals
6 Go-live/hypercare	Assess readiness, obtain cutover approval and monitor early issues.	Readiness and hypercare record

8. Flagship workflow — master data migration

Example: a new ERP customer uploads a customer master spreadsheet containing 5,000 records. UNIFY preserves the source, profiles the file, suggests mappings, applies deterministic validations, requests approval, migrates to sandbox and reconciles the outcome.



Exceptions return to correction; production migration is outside MVP.


Mandatory controls

Preserve original source; version mappings and transformations; maintain record-level source-to-target traceability; validate mandatory fields and references; execute in batches; use idempotent retries; reconcile counts and applicable financial totals; retain rejected records/reasons; require explicit approval before production migration.

PART C — TECHNICAL SOLUTION ARCHITECTURE

9. Detailed system architecture

Start with a modular monolith and independently running background workers. This is simpler to build and operate than a large microservice estate while preserving clear boundaries for later extraction.

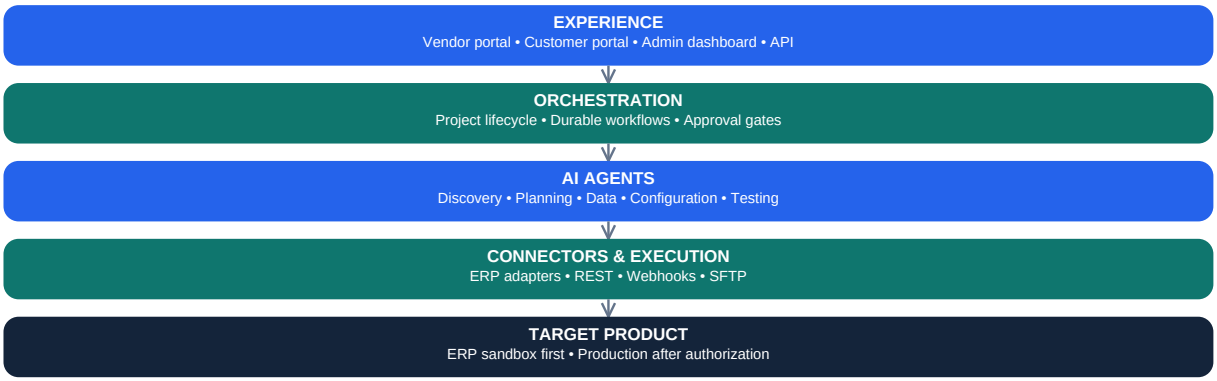

Component	Recommended technology	Responsibility
Web application	React / Next.js	Vendor/customer portals and dashboards.
Backend/API	Python / FastAPI	Business APIs, validation and authorization.
Identity	Keycloak or OIDC provider	Authentication, roles and sessions.
Primary database	PostgreSQL	Transactional and tenant-scoped data.
Vector retrieval	pgvector initially	Search over product docs and approved knowledge.
Workflow engine	Temporal	Durable state, retries, timers and recovery.
Agent orchestration	LangGraph	Agent reasoning, tool selection and human gates.
AI gateway	OpenAI API behind abstraction	Model access, routing, usage and policy.
File storage	S3-compatible storage	Uploads, reports and generated artifacts.
Monitoring	OpenTelemetry	Traces, metrics and diagnostics.

Temporal should own durable business workflow state, retries, timers, checkpoints and recovery. LangGraph should coordinate AI reasoning, context and tool selection within bounded tasks. They have complementary responsibilities.

10. Product connector architecture

The connector is the key to product independence. Every ERP adapter implements a standard contract and exposes only documented, allow-listed capabilities. AI must not invent API endpoints, database fields or configuration options.

Standard operations: authenticate(); get_product_metadata(); get_supported_modules(); get_entity_schema(entity); validate_records(entity, records); create_records(entity, records); update_records(entity, records); get_records(entity, filters); execute_configuration(config); execute_test(test_case); check_connection().

Capability registry: product/version, modules, entities, field metadata, endpoint references, supported operations, environments and permission scopes. This registry is the source of truth for agent execution.

11. Deployment environments

Environment	Purpose	Permitted actions
Development	Agent and connector development	Synthetic/test data only; no production credentials.
Sandbox	Customer implementation and verification	Approved test migrations and configuration.
Production	Live customer ERP	Explicitly authorized, least-privilege operations only.

PART D — DATABASE DESIGN

12. Database architecture and entity model

Use PostgreSQL as the primary transactional database. A vendor is a tenant; each tenant can register multiple products and onboard multiple customers; each customer can have multiple implementation projects.

TENANTS	→	**USERS / TENANT_USERS**		**PRODUCTS**
CUSTOMERS	→	**PROJECTS**	←	**PRODUCTS**
PROJECTS	→	**REQUIREMENTS / TASKS**	→	**AGENT_RUNS / ACTIONS**
PROJECTS	→	**MIGRATION_JOBS**	→	**MAPPINGS / BATCHES / RECONCILIATIONS**
PROJECTS	→	**CONFIG / INTEGRATIONS**	→	**TESTS / APPROVALS / AUDIT**

Core database tables

A. Tenant and user management

tenants (id, name, status, plan); users (id, email, name, status); tenant_users (tenant_id, user_id, role_id); roles; permissions; user_sessions.

B. Product management

products (tenant_id, name, version, status); product_modules; product_entities (schema_json); product_fields (data_type, required); product_capabilities; product_connectors; product_playbooks (versioned definition).

C. Customer and implementation

customers (tenant_id, customer_name, industry); customer_users; projects (tenant_id, customer_id, product_id, status); project_phases; project_tasks; project_dependencies; requirements; project_milestones; project_risks.

D. Documents and migration

uploaded_files (storage_key, checksum); file_sheets; data_profiles; migration_jobs; migration_mappings; migration_rules; migration_batches; migration_records; migration_reconciliations.

E. Configuration and integration

configuration_jobs; configuration_items; integration_connections; integration_mappings; integration_runs.

F. AI agent management

agent_definitions; agent_runs; agent_actions; agent_approvals; agent_memory; knowledge_documents; knowledge_chunks.

G. Testing and governance

test_cases; test_runs; approvals; audit_logs; notifications; usage_records.

Database design rules

1. Tenant-owned records carry tenant_id directly or inherit a strictly enforced tenant-scoped parent.
2. Use UUID primary keys and created_at / updated_at / created_by metadata.
3. Use JSONB for variable metadata, not to replace relational structure.
4. Store files in object storage, not database blobs.
5. Store secrets in a secrets manager, never ordinary configuration tables.
6. Version product schemas, playbooks, mappings and agent definitions.
7. Use append-only audit events for critical actions.
8. Enforce row-level security and tenant-scoped authorization.
9. Define retention, deletion and data export policies.
10. Separate source, transformation and target records for migration traceability.

Migration data layers

SOURCE Original Excel / CSV / external data
↓

TRANSFORMATION
Mapping • cleansing • conversion • validation


↓

TARGET
ERP sandbox / production

PART E — AI AGENT DESIGN

13. Agent architecture

Use specialized agents coordinated by an implementation orchestrator. The orchestrator delegates bounded work; the durable workflow engine owns project state and transitions. Agents share approved context but cannot bypass permissions or execute arbitrary operations.

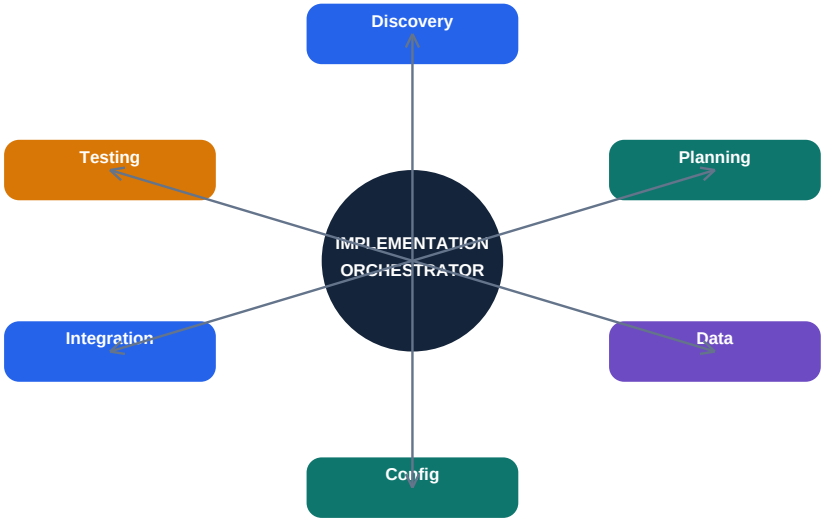

Agent	Responsibility	Primary output
Discovery	Extract/classify requirements; identify gaps and questions.	Reviewed requirements baseline.
Planning	Build phases, tasks, dependencies, owners and milestone suggestions.	Approved implementation plan.
Data migration	Profile, map, transform, validate, migrate and reconcile.	Sandbox migration report.
Configuration	Propose supported setup actions and verify resulting state.	Configuration evidence.
Integration	Configure and test supported external connections.	Integration test report.
Testing	Generate and execute requirement-linked scenarios.	Test execution evidence.
Go-live	Evaluate readiness conditions and blockers.	Readiness recommendation.
Hypercare	Classify issues and suggest approved knowledge-based resolutions.	Issue triage recommendations.

14. Agent workflow specifications

Discovery Agent: read requirement documents, extract and classify business requirements by ERP module, identify standard/gap/custom requirements, detect missing information, generate clarification questions, prepare fit-gap report and obtain consultant approval. Output is source-linked requirements with confidence and review status.

Planning Agent: use approved requirements, product playbook, customer complexity, modules, branches, migration volume, integrations and target dates. Generate tasks, dependencies, effort suggestions, owners, milestones and risks; request manager approval.

Data Migration Agent: perform file ingestion, schema detection, profiling, AI-assisted field mapping, deterministic validation/transformation, sandbox migration, reconciliation and exception handling. Ambiguous business meaning is escalated, not guessed.

Configuration Agent: derive setup from approved requirements; check capability registry and dependencies; propose values; obtain authorization; execute through connector; read back and verify; retain before/after evidence.

Integration Agent: inspect integration requirements and supported connector; validate API specification; request credential authorization; map fields; test connectivity and controlled transactions; validate responses and error handling; publish report.

Testing Agent: generate requirement-linked scenarios with preconditions, steps, expected results and test data; execute supported tests; capture actual results; record defects and retest.

Go-live Agent: evaluate migration reconciliation, configuration, integration, UAT, critical defects, access readiness and customer approval. It recommends readiness but does not authorize production activation.

Hypercare Agent: initially classify issues, search approved knowledge and propose resolutions for human review. Do not build a full autonomous support platform in MVP.

PART F — API AND INTEGRATION DESIGN

15. Core API design

Base URL: https://api.unify-platform.com/v1. Use REST conventions, JSON, versioning, tenant authorization, pagination, standardized errors and idempotency keys for write operations.

Module	Method	Endpoint	Purpose
Vendor	POST	/tenants	Register vendor tenant.
User	POST	/users	Create user.
Product	POST	/products	Register ERP product.
Product	GET	/products/{id}/capabilities	Retrieve capabilities.
Connector	POST	/connectors	Register connector.
Customer	POST	/customers	Register customer.
Project	POST	/projects	Create project.
Discovery	POST	/projects/{id}/discovery	Start discovery.
Planning	POST	/projects/{id}/plan	Generate plan.
Files	POST	/projects/{id}/files	Upload customer data.
Migration	POST	/projects/{id}/migrations	Create migration job.
Migration	POST	/migrations/{id}/validate	Validate data.
Migration	POST	/migrations/{id}/execute	Execute approved migration.
Configuration	POST	/projects/{id}/configurations	Create configuration job.
Integration	POST	/projects/{id}/integrations	Register integration.
Testing	POST	/projects/{id}/tests/run	Start test execution.
Approval	POST	/approvals/{id}/decision	Record approval.
Go-live	GET	/projects/{id}/readiness	Retrieve readiness.

Connectivity priorities

Method	Use case	Priority
REST APIs	ERP application operations.	P0
Webhooks	Status and event updates.	P0
SFTP	Legacy file exchange.	P1
Database connector	Approved legacy data extraction.	P1
UI automation	Products without usable APIs; controlled use.	P2
MCP	Standardized agent tool access where useful.	P2

Start with REST APIs and webhooks. Database access and UI automation add security and reliability risks and should not be required for the first ERP pilot.


PART G — SECURITY, GOVERNANCE AND RELIABILITY

16. Security requirements

Area	Requirement
Authentication	OAuth 2.0 / OpenID Connect; secure session lifecycle.
Authorization	RBAC plus tenant, project, environment and action-level permissions.
Tenant isolation	Tenant-scoped access and PostgreSQL row-level security.
Encryption	TLS in transit and encryption at rest.
Credentials	Dedicated secrets manager; short-lived credentials where supported.

Area	Requirement
File security	File type/size validation, malware scanning and restricted parsing.
AI security	Treat uploaded documents as untrusted; prompt-injection controls and tool allow-lists.
Audit	Append-only event history for approvals, reads/writes and critical actions.
Retention	Configurable retention, deletion and export policies.
Recovery	Backups, restore tests, checkpoints and recovery procedures.
Production	Least privilege and explicit authorization for production-impacting actions.

17. Human approval and execution lifecycle



Activity	Approval policy
Document classification / profiling	Automatic processing; review uncertain findings.
Requirements and plan	Consultant / manager approval before baseline.
Field mapping / transformation	Specialist approval for ambiguous or material mappings.
Sandbox migration / configuration	Authorized project approval and logged execution.
Production migration / go-live	Explicit authorized approval; not autonomous in MVP.

PART H — DEVELOPMENT BACKLOG

18. Agile epics

Epic	Description	Priority
EPIC-01	Multi-tenant platform foundation.	P0
EPIC-02	Vendor and product registry.	P0
EPIC-03	ERP connector framework.	P0
EPIC-04	Customer onboarding.	P0
EPIC-05	AI discovery and planning.	P0
EPIC-06	File ingestion and data profiling.	P0
EPIC-07	AI data mapping and migration.	P0
EPIC-08	Configuration execution.	P1
EPIC-09	Integration framework.	P1
EPIC-10	Testing and validation.	P1
EPIC-11	Approval, audit and governance.	P0
EPIC-12	Go-live and hypercare.	P2

19. Key user stories and acceptance criteria

US-001 Vendor registration

Vendor registers on UNIFY. **Acceptance:** Tenant created; admin assigned; data isolated; secure login works.

US-002 Role-based access

Admin assigns roles to users. **Acceptance:** Backend permissions enforced; unauthorized actions rejected and logged.

US-003 Register ERP product

Admin registers product/version and modules. **Acceptance:** Product metadata, modules, entities and capabilities stored; activation supported.

US-004 Configure ERP connector

Admin configures connector. **Acceptance:** Credentials secured; connection test works; capabilities detected; failures logged.

US-005 Create customer

Manager creates customer implementation. **Acceptance:** Customer details and product captured; project created; customer admin invited.

US-006 Submit requirements

Customer submits requirements and documents. **Acceptance:** Inputs accepted; mandatory gaps highlighted; history retained.

US-007 Requirement extraction

AI extracts requirements. **Acceptance:** Source-linked requirements; module classification; uncertainty flags; consultant review.

US-008 Generate plan

AI generates plan from approved requirements. **Acceptance:** Tasks/dependencies generated; owners/dates suggested; manager approval before publish.

US-009 Upload master data

Customer uploads Excel/CSV. **Acceptance:** Supported files upload; invalid formats rejected; original preserved; project association correct.

US-010 Data profiling

Specialist identifies data quality issues. **Acceptance:** Counts calculated; mandatory gaps and duplicates flagged; report downloadable.

US-011 AI field mapping

AI recommends source-to-target mappings. **Acceptance:** Rationale and confidence shown; ambiguous mappings reviewed; versions retained.

US-012 Execute migration

Authorized consultant migrates approved data. **Acceptance:** Approved mappings only; batches; failures captured; reconciled; safe retries.

US-013 Configuration recommendation

AI recommends supported configuration. **Acceptance:** Capabilities/dependencies checked; approval before execution; result verified.

US-014 Integration connectivity

Consultant registers/tests API integration. **Acceptance:** Credentials securely referenced; connectivity/mappings validated; history retained.

US-015 Generate test scenarios

QA generates tests from requirements. **Acceptance:** Tests link to requirements; preconditions/expected results; QA can edit.

US-016 Go-live readiness

Manager requests readiness report. **Acceptance:** Migration, defects and UAT checked; blockers listed; production requires authorization.

PART I — TESTING AND PRODUCT ACCEPTANCE

20. MVP acceptance tests

ID	Scenario	Expected result
TC-001	Register ERP vendor	Tenant successfully created.
TC-002	Register ERP product	Capabilities recorded.
TC-003	Connect mock ERP	Connection validated.
TC-004	Onboard customer	Project generated.
TC-005	Upload requirements	Requirements extracted and source-linked.
TC-006	Generate plan	Tasks and dependencies created.
TC-007	Upload customer master	File processed and preserved.
TC-008	Validate customer data	Data-quality report generated.
TC-009	Map source fields	Reviewable mappings generated.
TC-010	Migrate records	Sandbox records created through authorized connector.
TC-011	Reconcile migration	Source/target reconciliation recorded.
TC-012	Execute configuration	Supported settings verified.
TC-013	Execute test cases	Results and evidence captured.
TC-014	Assess readiness	Readiness report generated.
TC-015	Unauthorized execution	Access denied and logged.
TC-016	Retry failed batch	No unintended duplicate records.
TC-017	Cross-tenant access	Access denied.

Pilot exit criteria


- Every migrated record has source traceability or an explicit exception.
- Every production-impacting action requires authorization.
- No cross-tenant data leakage in security testing.
- Mandatory migration reconciliation checks pass before migration is declared complete.
- Critical test scenarios are executed and evidenced.
- Implementation managers can identify blockers from a single dashboard.
- At least two customer implementation projects are completed through the pilot workflow.

Avoid an arbitrary aggregate accuracy target that hides material errors. Critical financial and master data must satisfy applicable mandatory validation and reconciliation rules.

PART J — PRODUCT DASHBOARD AND USER EXPERIENCE

21. Proposed application screens

The experience should be organized around implementation lifecycle and exception management—not internal agent names. Vendors should see customer projects, status, approvals, risks and outcomes in one workspace.

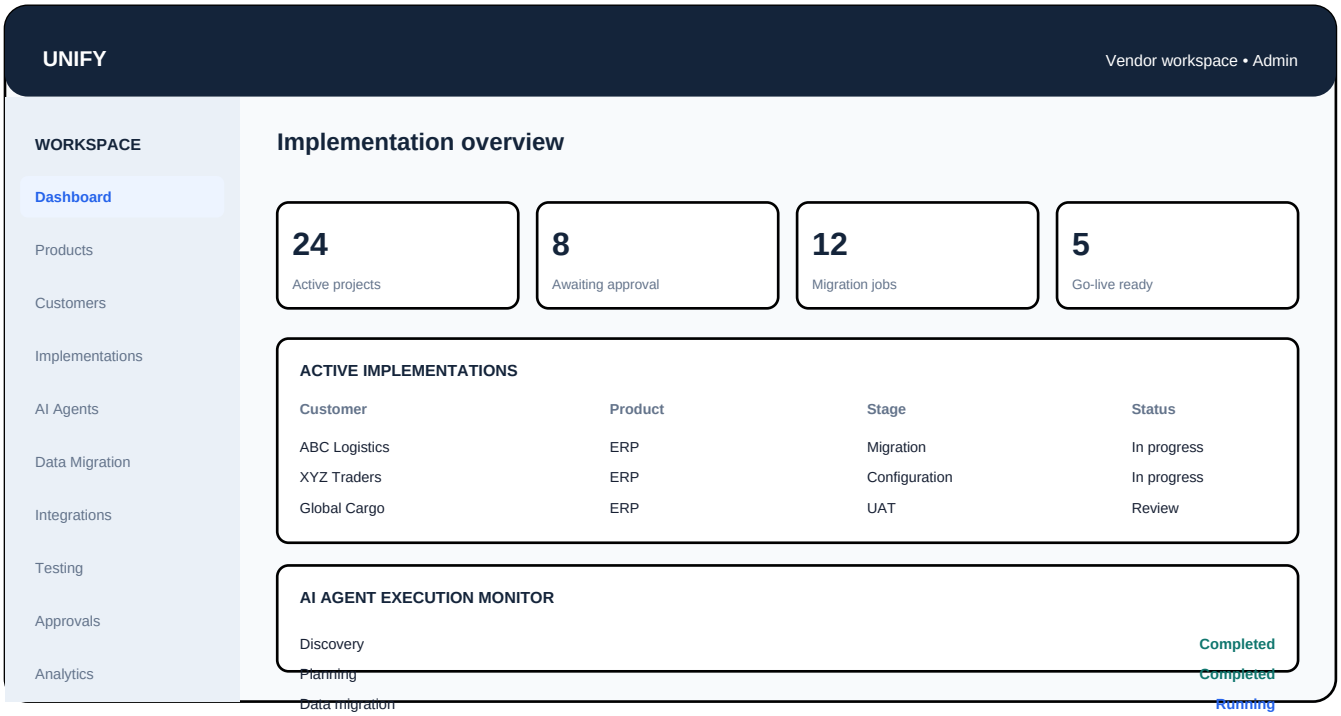

Illustrative dashboard; counts and customer names are sample data, not live platform metrics.

Primary navigation

Dashboard • Products • Customers • Implementations • AI Agents • Data Migration • Integrations • Testing • Approvals • Analytics • Settings.

Project workspace should show customer/product details; lifecycle stage; milestone progress; tasks and dependencies; agent execution status; pending approvals; migration quality; integration health; test results; blockers; and audit history.

PART K — PRODUCT SUCCESS METRICS

22. KPIs to measure

KPI	Definition / measurement
Implementation cycle time	Elapsed days from kickoff to agreed go-live or completion.
Automation coverage	Eligible activities completed by controlled automation divided by eligible activities.
Human intervention rate	Manual corrections, decisions and approvals per project.
Data migration accuracy	Correctly migrated records against verified source and business rules.
Migration exception rate	Records requiring correction or manual handling.
First-time-right configuration	Configuration actions passing initial verification.
Integration success rate	Successful validated integration transactions / attempts.
Test pass rate	Passed test cases / executed test cases.
Go-live readiness	Mandatory readiness conditions satisfied with evidence.
Cost per implementation	Total delivery cost per successfully implemented customer.

The most commercially important metric is cost per successfully implemented customer. It connects platform outcomes to vendor delivery economics.

PART J1 — VENDOR DASHBOARD

A dedicated vendor-facing workspace in UNIFY. This is distinct from the internal admin / implementation dashboard: it gives each ERP vendor or implementation partner a controlled view of its own products, customer projects, actions, evidence and performance.

1. Vendor dashboard — proposed home screen

UNIFY / VENDOR WORKSPACE — **Acme ERP Partner** | Vendor Admin | Help

Overview Products Customers Projects Integrations Documents Support

08	14	03	02	96%
Active projects	Customer accounts	Actions due	Open escalations	SLA compliance

PROJECT DELIVERY	STATUS	NEXT ACTION	DUE
Northstar Logistics — ERP rollout	In progress	Confirm migration mapping	04 Nov
Apex Components — Finance	At risk	Resolve API test failures	02 Nov
Bluewave Freight — WMS	On track	Submit UAT evidence	06 Nov
Orion Traders — Go-live	Awaiting customer	Review sign-off	08 Nov

VENDOR ACTION CENTRE

- 2 documents require renewal
- 1 customer approval pending
- 3 implementation tasks due this week
- 1 integration credential expires soon

RECENT ACTIVITY

- Mapping file uploaded — 09:42
- UAT evidence accepted — yesterday
- Support case updated — 29 Oct

Illustrative screen and sample values only. Live figures must be calculated from tenant-scoped project, task, SLA and document records.

2. Vendor dashboard modules and capabilities

Module	Vendor capabilities	UNIFY controls
Company profile & users	Maintain company contacts, delivery locations, support contacts and named users; invite or deactivate team members.	Vendor verification, role-based access, approval of profile changes.
Products & capabilities	Register ERP products, editions, modules, supported versions, hosting models, regions and implementation capabilities.	Product claims reviewed; version and capability history retained.
Customer accounts & projects	See only assigned customers/projects; view lifecycle stage, milestones, risks, dependencies and customer actions.	Assignment-based access; customer data isolated by tenant and project.

Module	Vendor capabilities	UNIFY controls
Implementation tasks	Accept tasks, assign vendor resources, update progress, add comments and upload evidence.	Due dates, required evidence, approval gates and audit trail.
Integrations & environments	Register connector endpoints, supported APIs, sandbox details and integration status; submit test results.	Secrets never displayed after entry; credentials stored in vault; scoped access.
Documents & compliance	Upload contracts, security documents, product guides, certificates and implementation templates; track expiry.	Document type, owner, expiry reminders, review and version history.
Support & escalations	Raise cases, attach logs, view case status, respond to questions and escalate delivery blockers.	Severity, SLA clock, routing, escalation policy and case history.
Performance & analytics	Review project completion, milestone adherence, defect trends, response times and customer feedback.	Metric definitions, date filters, explainable calculations and export permissions.

PART J2 — VENDOR WORKFLOWS & MVP SCOPE

3. Core vendor journeys

Journey	Vendor action	UNIFY response / control
Vendor registration	Submit company details, contacts, legal/compliance documents and nominate vendor admin.	Create pending vendor record; validate mandatory fields; internal UNIFY admin approves before access is activated.
Product onboarding	Add ERP product, modules, versions, hosting options, API documentation and supported migration formats.	Create product capability profile; flag missing evidence; review and publish approved catalogue entry.
Project assignment	Accept assigned customer project, confirm delivery lead and resource plan.	Grant access only to assigned project and minimum necessary customer data.
Implementation execution	Complete assigned discovery, configuration, migration, integration, testing and training tasks; upload evidence.	Track milestones; validate required evidence; route customer / UNIFY approvals; record audit events.
Issue resolution	Raise or respond to support case; attach diagnostic files and provide remediation update.	Apply severity and SLA; notify owner; escalate overdue or blocked cases.
Project closure	Submit final checklist, handover documents and vendor completion confirmation.	Verify mandatory deliverables; collect customer acceptance; close project and calculate performance metrics.

4. Roles, permissions and data boundaries

Role	Allowed actions	Restrictions
Vendor Admin	Manage vendor profile, invite vendor users, manage product submissions, view all projects assigned to that vendor.	Cannot view other vendors; cannot approve its own compliance or UNIFY-controlled milestones.
Vendor Project Lead	Manage assigned project team, tasks, milestones, comments and evidence.	Only assigned projects and customer data; no vendor-wide security or billing settings unless separately granted.
Vendor Contributor	Update assigned tasks, upload permitted evidence and respond to comments.	No user administration, project reassignment, approvals or access to unrelated projects.
Vendor Support Agent	View and respond to support cases routed to the vendor; attach diagnostics and remediation notes.	Only support-related data required to resolve the case.
UNIFY Admin / Reviewer	Approve vendor, product and compliance records; assign projects; review evidence; manage escalations.	Privileged actions require audit logging and least-privilege access.

5. Vendor dashboard KPIs

• **Delivery:** active projects, projects by stage, milestone completion rate, on-time milestone rate, go-live readiness.

• **Quality:** open defects by severity, defect ageing, UAT pass rate, re-open rate, post-go-live issues.

• **Responsiveness:** support first-response time, resolution time, SLA compliance, overdue actions.

• **Compliance:** documents pending review, documents expiring in 30/60/90 days, unresolved security findings.

• **Customer outcomes:** customer acceptance status, CSAT (when collected), handover completeness.

Metric rule: define numerator, denominator, time window, exclusions and source record for every KPI. Do not display a composite vendor score until pilot data proves the weighting is fair and comparable across vendor types.

6. Recommended MVP acceptance criteria

1. A vendor admin can register, submit required documents and see approval status.

2. A vendor can register a product and submit capability / integration information for UNIFY review.

3. Vendor users can see only projects explicitly assigned to their vendor and role.

4. Vendor project leads can update assigned tasks, milestones and evidence; required approvals remain with the designated customer or UNIFY approver.

5. The dashboard shows accurate project, task, SLA and document counts using tenant-scoped data.

6. Expired or soon-to-expire documents and overdue actions appear in the action centre with clear owners and due dates.

7. All privileged changes, approvals, uploads and status changes are timestamped and attributable to a user.

8. Vendor access can be suspended or revoked without deleting the audit history.

7. Recommended implementation sequence


Release	Include	Why this order
MVP 1	Vendor registration, profile, users, product catalogue, project assignments, task updates, evidence uploads, role controls.	Creates the secure vendor collaboration foundation and enables the first pilot.
MVP 2	Integration details, document expiry, support cases, SLA tracking, notifications and audit exports.	Adds operational governance and reduces manual follow-up.
Later	Vendor benchmarking, advanced analytics, resource capacity, commercial / invoice workflows, automated compliance checks.	Requires stable usage data, agreed metric definitions and validated commercial need.

Product decision to validate: confirm whether the first vendor dashboard is for ERP software vendors, implementation / system-integration partners, or both. If both, use a shared portal shell with vendor-type-specific onboarding fields, capabilities and performance measures. Avoid exposing customer commercial terms, other vendors' data, internal UNIFY notes or secrets.

PART L — DEVELOPMENT AND DELIVERY ROADMAP

23. Six-month MVP roadmap

Indicative 24-week plan, assuming an experienced small team, timely ERP sandbox/API access and an engaged pilot vendor. Rebaseline dates after discovery and resource confirmation.



Month	Focus	Key work	Exit deliverable
1	Foundation	Architecture, tenancy, identity, roles, product registry, connector contract and mock ERP.	Vendor registers product and tests connector.
2	Discovery & planning	Customer onboarding, document ingestion, discovery agent, requirements and plan generation.	Approved implementation blueprint.
3	Migration	Excel/CSV, profiling, mapping, validation, transformation, sandbox migration and reconciliation.	Traceable sandbox migration.
4	Configuration & integration	Supported configuration actions, REST integrations, webhooks and execution logging.	Controlled configuration and integration test.
5	Testing & readiness	Requirement-linked tests, approvals, exception handling, audit and readiness report.	End-to-end controlled workflow.
6	Pilot & hardening	Connect real ERP sandbox, run pilot projects, measure outcomes and improve security/usability.	Pilot-ready MVP and evidence-based decision.

Delivery gates

Gate 1 — Month 1: tenant isolation, product registry and mock connector demonstrated.
Gate 2 — Month 2: requirements and plan reviewed by practitioners.
Gate 3 — Month 3: sandbox migration and reconciliation demonstrated.
Gate 4 — Month 5: end-to-end controlled workflow passes acceptance tests.
Gate 5 — Month 6: pilot evidence supports go / revise / stop.

24. Team and indicative budget

Role	Allocation	Responsibility
Product / implementation architect	1; founder-led or full-time	Product strategy, methodology, acceptance criteria and pilot.
AI / backend engineers	2	Agent runtime, APIs, workflows and data services.
Full-stack engineer	1	Vendor/customer portals and dashboards.
Integration engineer	1	ERP adapter, API connectivity and sandbox execution.
QA / automation engineer	1	Testing, migration validation and release quality.
UX designer	Part-time	User experience and interaction design.

Indicative six-month budget — India-based lean team

Cost category	Range	Notes
Engineering team	₹30–45 lakh	Depends on hiring mix, seniority and founder contribution.
Cloud and AI infrastructure	₹2–5 lakh	Early environments, model usage and storage.
Security and testing	₹2–4 lakh	Security review, testing tools and remediation.
Design, legal and miscellaneous	₹2–4 lakh	UX, contracts and operating expenses.
Indicative total	₹36–58 lakh	Excludes major certification and substantial sales expenditure.

Planning estimates only—not quotations or approved funding requirements. Validate through hiring plans, architecture choices and a scoped proof of concept.

25. Pilot design and commercial validation

Secure one ERP vendor design partner with sandbox access and API documentation. Select two or three real customer implementation cases, initially focusing on customer, vendor and item master migration. Record current manual baseline before UNIFY, then compare effort, elapsed time, quality, exceptions and rework.

Pilot measure	Evidence
Effort reduction	Consultant hours per activity before vs after UNIFY.
Migration quality	Traceability, rejected records, duplicate prevention and reconciliation.
Cycle time	Elapsed time from file receipt to approved sandbox migration.
Intervention rate	Human corrections and approvals per run.
Reliability	Failures, retries, recovery time and audit completeness.
Commercial intent	Willingness to pay, procurement path, pilot conversion and annual contract potential.

26. Key risks and mitigations

Risk	Impact	Mitigation
Limited ERP API access	Cannot reliably execute supported operations.	Secure design partner/API contract early; start with mock connector.
Inconsistent customer data	AI may misinterpret ambiguous business meaning.	Deterministic rules, exception queue, traceability and specialist approval.
Unsafe agent execution	Incorrect writes may affect operational/financial records.	Allow-listed tools, least privilege, sandbox-first, approvals and audit.
Tenant data leakage	Cross-vendor data exposure.	Tenant-scoped authorization, RLS, security tests and isolation review.
Scope expansion	Universal support delays proof of value.	One ERP connector and limited entities for MVP.
Unproven willingness to pay	Technical success may not translate to adoption.	Vendor interviews, quantified baseline and pilot commitments.

27. Five assumptions that need validation

These assumptions should be tested before committing to the full six-month build and budget. They separate technical feasibility from customer demand and delivery readiness.

#	Assumption	How to validate
1	The first ERP vendor will provide API documentation and sandbox access.	Secure a design partner; inspect API coverage, rate limits, authentication, test data and write operations.
2	The ERP vendor is willing to standardize at least some implementation workflows.	Interview implementation leaders; map repeated tasks and agree reusable playbooks and validation rules.
3	Customer master data is available in Excel or CSV.	Review representative anonymized files from pilot customers; assess format variation and data quality.
4	Product configuration operations can be exposed through supported APIs.	Run a technical spike against ERP sandbox; verify read/write capability, permissions and read-back.
5	There is a measurable financial incentive for vendors to adopt a separate implementation platform.	Establish current implementation hours/cost, rework and cycle time; test willingness to pay and pilot conversion.

Recommended validation sequence

1. Conduct 5–8 structured interviews with ERP vendor leaders and implementation managers.
2. Select one design partner and obtain agreement for discovery/pilot access.
3. Review API documentation and representative anonymized migration files.
4. Build a narrow technical proof: field mapping → deterministic validation → approved sandbox migration → reconciliation.
5. Compare baseline delivery effort with pilot results and test commercial willingness to pay.

Stakeholder decision requested

Approve a time-boxed discovery and technical proof of concept—not an unconditional commitment to the entire six-month build. Proceed to full MVP only when ERP connectivity, reliable migration, controlled execution and vendor demand have been demonstrated.

UNIFY — One engine. Any product. Automated implementation.

Consolidated stakeholder discussion draft • 31 October 2026. Product name, market position, scope, estimates, dates and targets are proposals requiring validation.
